

PROJECT MANAGEMENT · TEAM 05

The Journey

Renewal of the Assembly Workshop

A guided walk-through of the project plan — from business need to a Go / No-Go decision.

Shandong Productions · Shanghai · “Move Up Our Brand”



Lorenzo · Matteo · Ilaria · Samuele · Mariachiara · Silvia · Simone

The Mission

Why we set out — the business need that anchors every decision ahead.

Renewal of the Assembly Workshop

A strategic initiative within the “Move Up Our Brand” program: modernise the Shanghai line to lift output and cut the CO₂ footprint, while improving the workforce environment.

PROJECT GOALS



+30%

Assembly capacity: 1,000 → 1,300 units/yr



-20%

Energy consumption reduction



20°C ±2°C

New HVAC climate control

THE RULES OF THE ROAD

Business constraints



€315k

Max project cost



€35k

Management reserve (€350k total)



≤4 wks

Production interruption



21 wks

Duration (incl. 2-wk CNY holiday)



≤€25k/yr

Maintenance cost

The Map

One project, four chapters — 19 working weeks across a 21-week calendar (incl. the 2-week Chinese New Year shutdown).

PERIOD 01

Foundation & Design

WBS Phases 1–2 · W1–W9



PERIOD 02

Sourcing & Site Prep

WBS Phases 3–4 · W9–W11



PERIOD 03

Installation

WBS Phase 5 · W11–W16



PERIOD 04

Testing & Handover

WBS Phases 6–7 · W17–W19



CNY shutdown · 2 wks

€315k

Total cost

4,050 h

Total effort

21 wks

Calendar

GO ?

Decision ahead

The Charter

The mandate we carry on the journey — scope, success criteria, and the team behind the wheel.

IN SCOPE

- Replace 5 assembly machines with new-generation units
- Turn-key HVAC climate-control system (first-of-type)
- Roof insulation + 15 high-efficiency windows
- Layout, electrical/fluids & conveyor re-routing (in-house)

SUCCESS CRITERIA

-  Capacity +30% (1,300 u/yr)
-  Energy –20%
-  HVAC 20°C ±2°C
-  On budget ≤ €315k & ≤ 21 wks

WHO STEERS

Governance & sponsor

- **Project Sponsor**
Approves budget & Go/No-Go
- **Project Manager**
Plan, schedule, cost & risk control
- **Technical Manager**
Authority over all engineering work
- **Procurement Manager**
Yangtze & HVAC vendor contracts

Foundation & Design

WBS Phases 1–2 · Initiation, planning, and full engineering design

TIMELINE

W1–W9

25 Jan 2027 → 09 Apr 2027



WHO LEADS

RAM

Technical Manager (+ PM)

Accountable for this leg



COST OF THIS LEG

€48.3k

PM Team: €31.1k · Engineering: €17.2k



EFFORT

968 h

Top: Project Manager (405h)

CUMULATIVE SPEND

35.9%

€113.2k of €315k by end

THIS LEG ON THE PROJECT TIMELINE





MILESTONE Plan approved (5 Feb) · Design complete (9 Apr)

Sourcing & Site Prep

WBS Phases 3–4 · Procurement of machinery, HVAC & materials; workshop cleared

TIMELINE

W9–W11

05 Apr 2027 → 23 Apr 2027



WHO LEADS

RAM

**Procurement Manager
(+ Technical Mgr)**

Accountable for this leg



COST OF THIS LEG

€150.4k

Materials: €124k · Installation: €13.1k



EFFORT

606 h

Top: Internal Workforce (250h)

CUMULATIVE SPEND

68.6%

€216k of €315k by end

THIS LEG ON THE PROJECT TIMELINE





MILESTONE Procurement done · Production STOP begins

Installation

WBS Phase 5 · Facilities, machinery, conveyors & control software installed

TIMELINE

W11–W16

19 Apr 2027 → 28 May 2027



WHO LEADS
RAM

Technical Manager

Accountable for this leg



COST OF THIS LEG

€79.2k

Installation: €50.9k · Engineering: €20.5k



EFFORT

1,720 h


Top: Internal Workforce (1040h)

CUMULATIVE SPEND

88.2%

€278k of €315k by end

THIS LEG ON THE PROJECT TIMELINE





MILESTONE Production STOP ends (14 May) · Install complete (28 May)

Testing & Handover

WBS Phases 6–7 · Commissioning, validation, training & final acceptance

TIMELINE

W17–W19

31 May 2027 → 18 Jun 2027



WHO LEADS

RAM

Technical Manager (+ PM)

Accountable for this leg



COST OF THIS LEG

€37k

Engineering: €15k · Tests & Delivery: €9k



EFFORT

756 h

Top: Commissioning Spec (170h)

CUMULATIVE SPEND

100%

€315k of €315k by end

THIS LEG ON THE PROJECT TIMELINE







MILESTONE Final Acceptance / GO-live (18 Jun)

The Money Story

How spend accumulates along the journey — and where every euro goes.

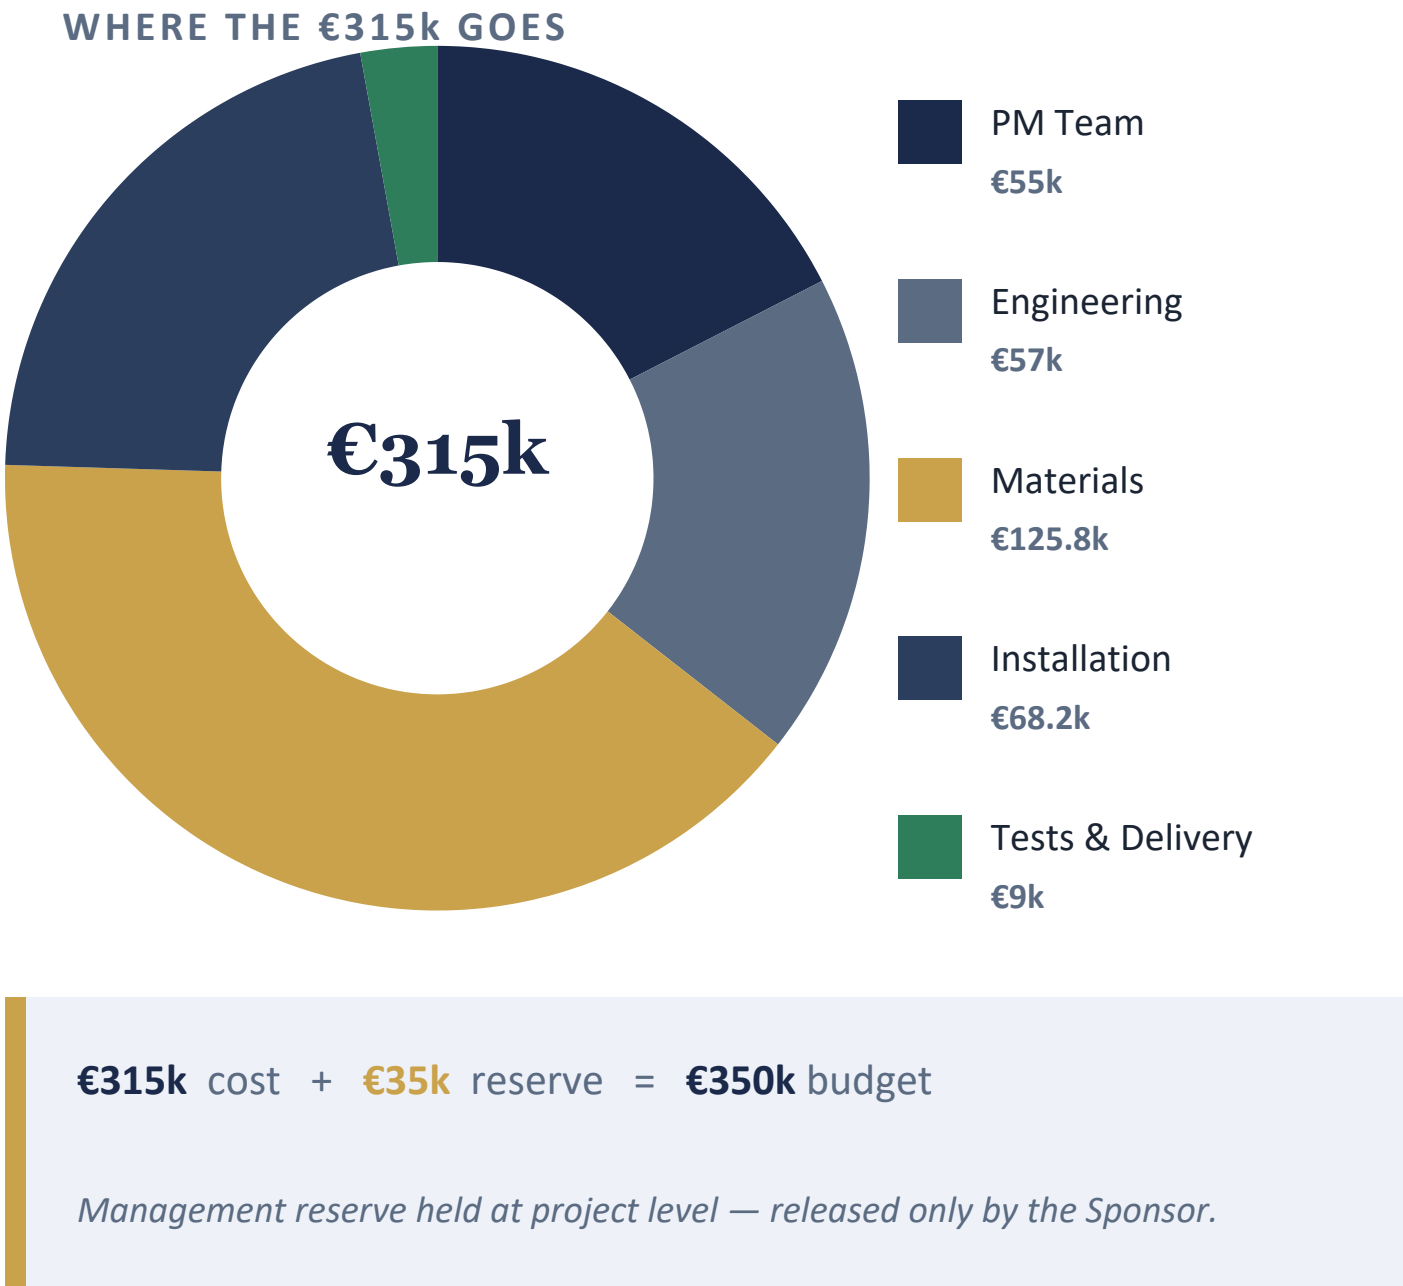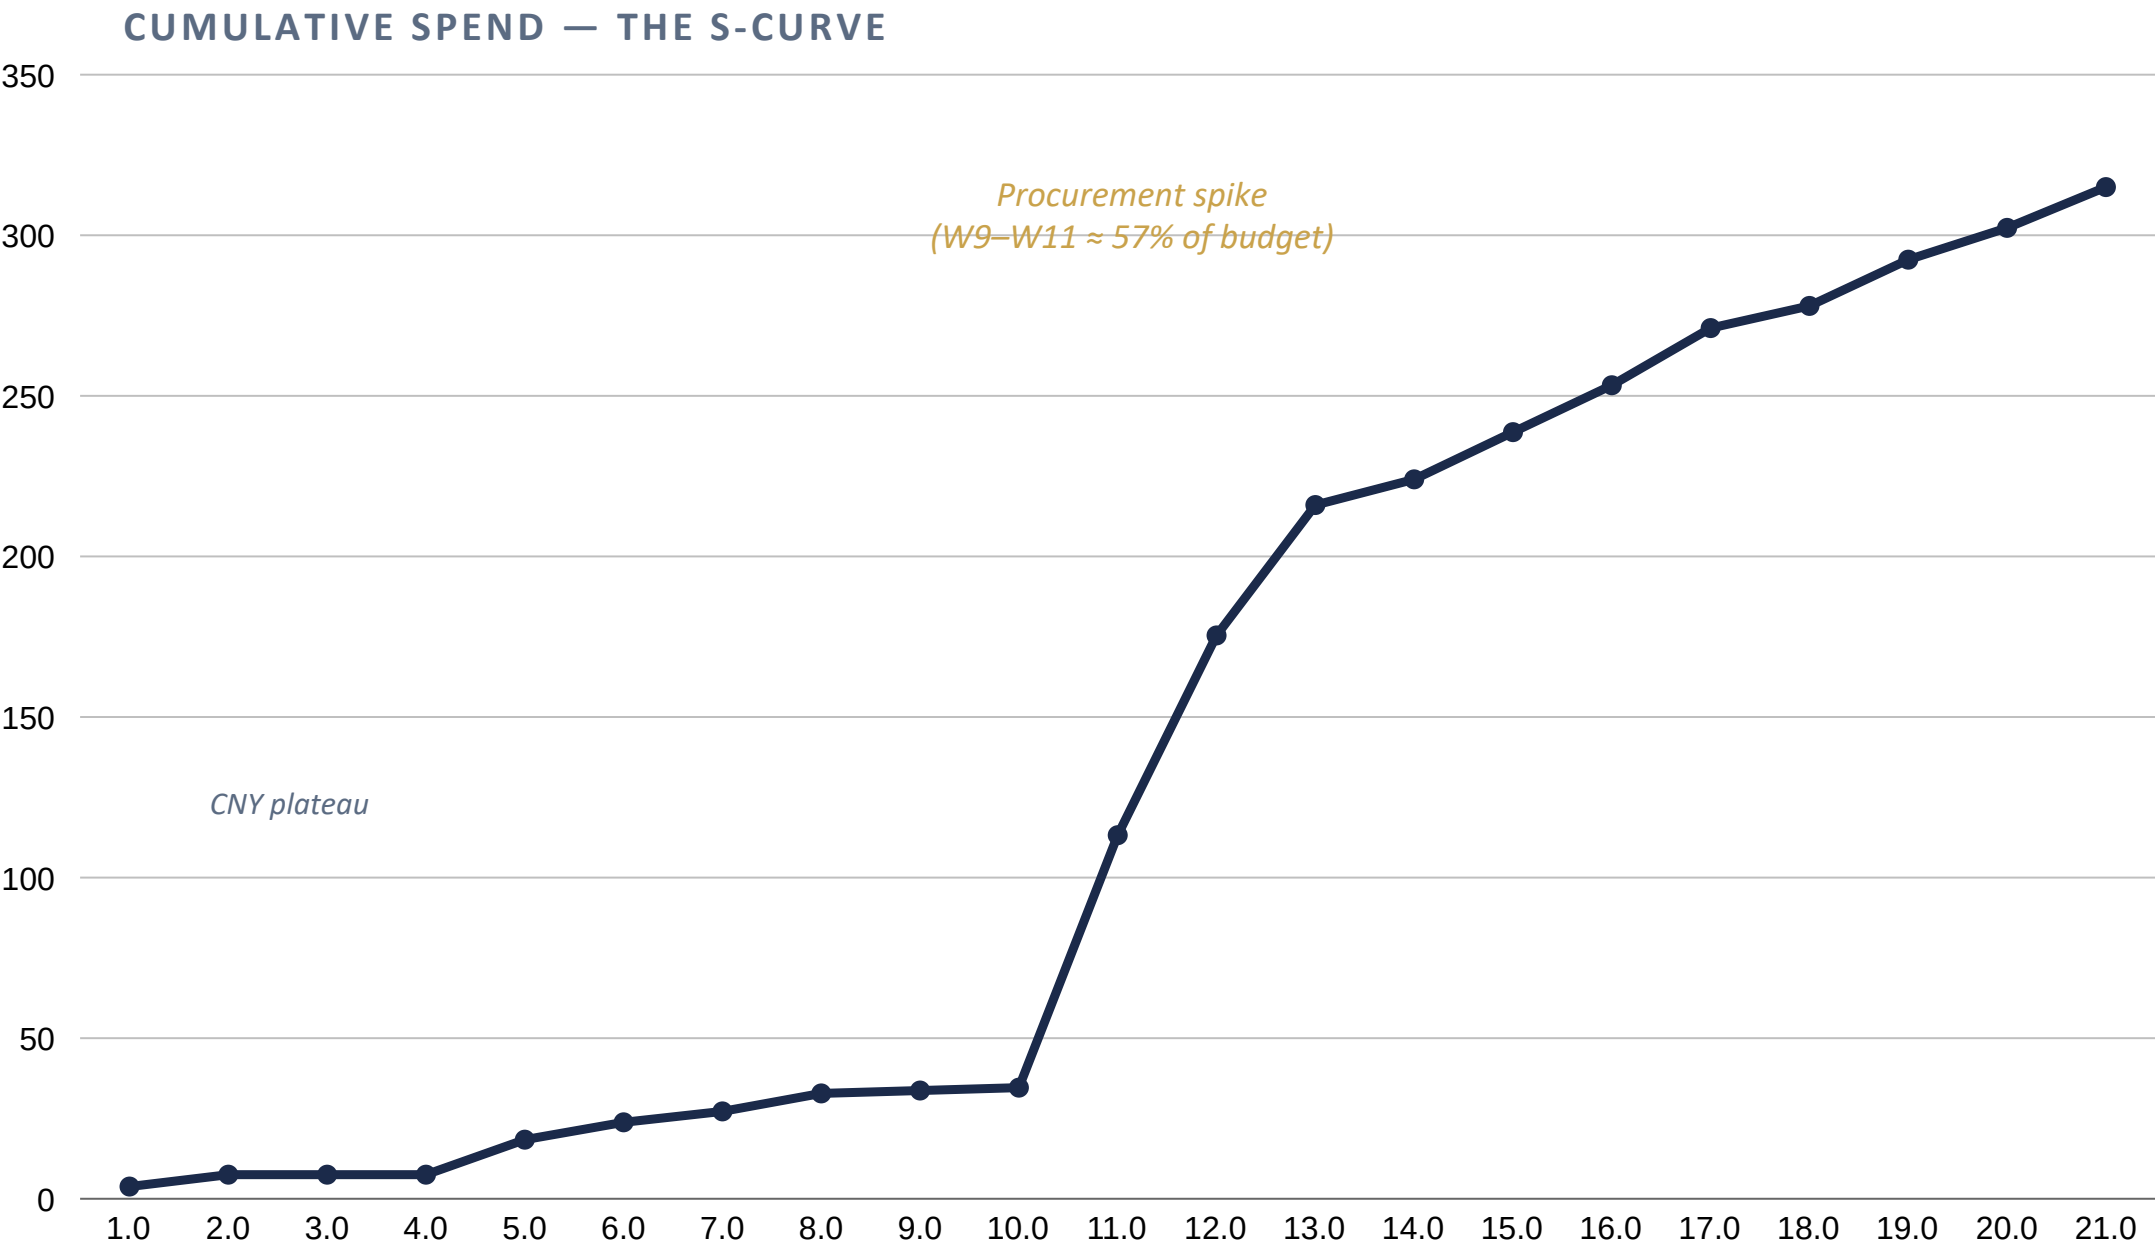

The Verdict

Every target met within budget and schedule. Our recommendation to the Sponsor:

✓	Capacity +30%	1,000 → 1,300 u/yr	Met by design
✓	Energy –20%	HVAC + insulation + windows	Met by design
✓	Climate 20°C ±2°C	Turn-key HVAC	Met by design
✓	Cost ≤ €315k	€315.0k planned	On budget
✓	Duration ≤ 21 wks	19 work + 2 CNY = 21	On schedule
✓	Interruption ≤ 4 wks	4-week stop (W11–W14)	Within limit



All success criteria satisfied · €35k reserve protects against the HVAC first-of-type risk.

Thank you

Questions & discussion — Team 05

Renewal of the Assembly Workshop · “The Journey” · Project Management Module

